




*The Skating Club of Boston*

# MILESTONE OF THE WEEK

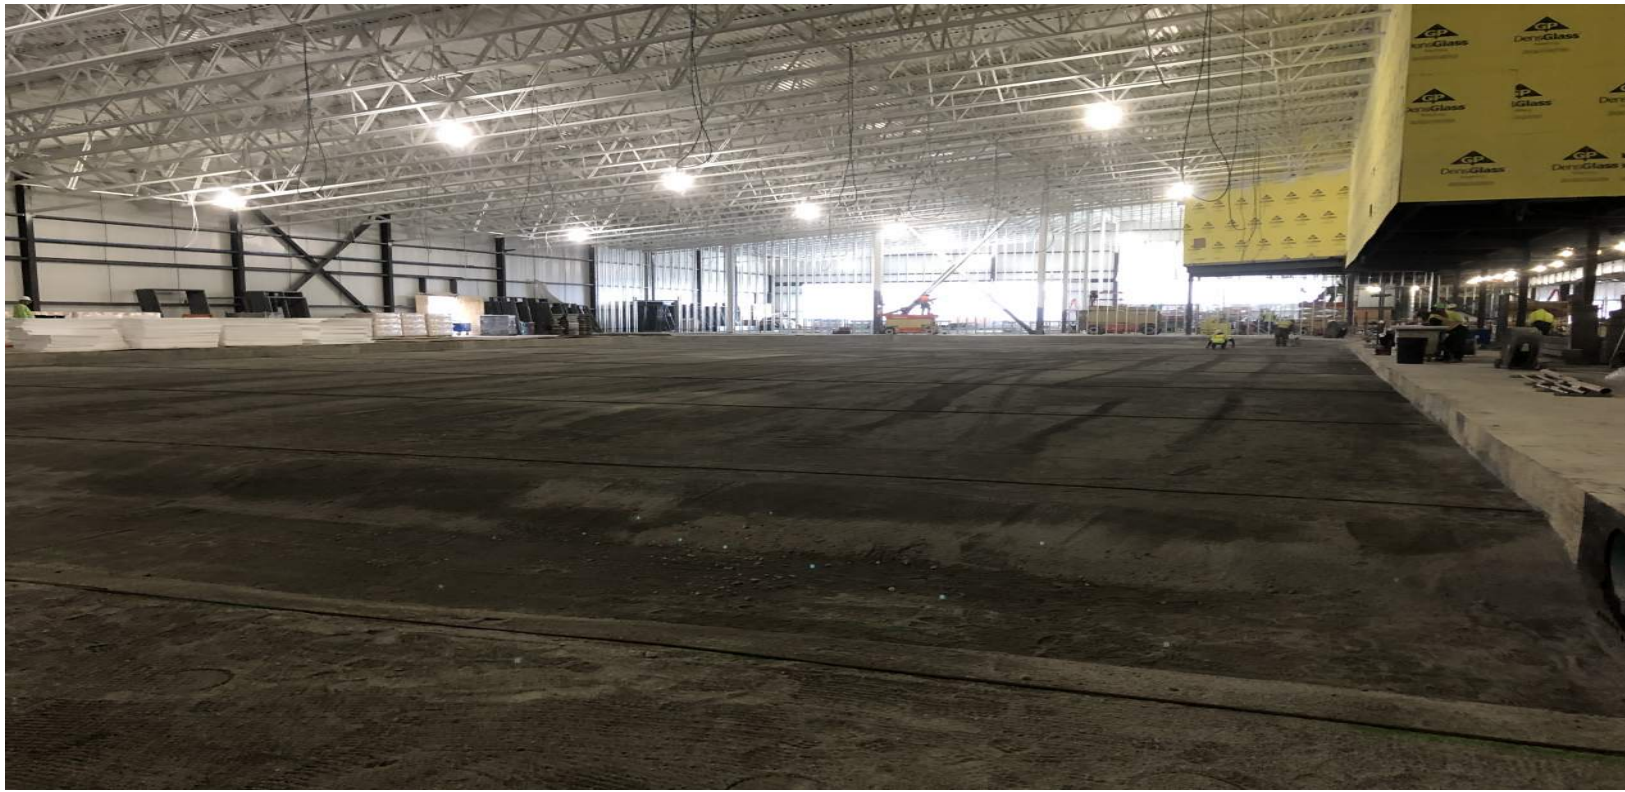

**January 24th, 2020**

## PROJECT FACTS

- Days On Site: **214**
- Percentage of roof installed: **99%**
- Cameras on-site: **3**
- Percentage of Panels installed: **97%**
- Manpower on-site: **130**
- Heavy Equipment Vehicles: **25+**

This week's milestone focuses on the West Figure-Skating Rink being several steps closer towards showcasing a pristine sheet of ice. To lay the foundation for the rink, crews imported a soil base that was compacted and leveled using an advanced laser leveling system. Then, six inches of compressed, crushed stone was laid and leveled, also by laser, to support the first set of rink pipes that will control the temperature in the rink bed. The next stage will be to lay the sand and the refrigeration pipes before pouring the concrete that will support the new ice. There's no doubt skating in Norwood will be coming soon!

**Stay tuned for more weekly updates!**



**JC&A**  
J. CALNAN & ASSOCIATES  
CONSTRUCTION MANAGERS | EST. 1996
